LIVERPOOL CENTRAL SCHOOL DISTRICT

PHASE 3 & 4 CAPITAL PROJECT CONSTRUCTION PROGRESS REPORT

NOVEMBER 5, 2020

LeCHASE

EXECUTIVE SUMMARY

PROGRESS

PHASE 3

Liverpool High School

- Athletics
  - The elevator was completed and ready for inspection.
  - Completed various interior finish work including painting, solid surface material, main entry stair flooring, wood mural and logo, display case trim, entry walk off mats, lobby markerboard material
  - Completed Walking track flooring and striping
  - Installed Gymnasium Bleachers and projector
  - Installed Athletic Equipment
  - Completed Ceilings, Lighting, and fixtures
  - Completed balance of Windows
  - Completed Sitework Finishes
  - Completed Doors and Harware
  - Completed systems commissioning
  - Completed final clean
  - Moved in of owner furnishings
  - Plumbing contractor completed bathroom and lockerroom fixture installation, commercial sink at the concession area
  - HVAC contractor completed grilles and diffuse installation, controls, and balancing
  - Fire alarm devices and public address system were completed
  - Electrical contractor completed wire pulling, outlets, switches, and trim, lighting installation, power to equipment

- Fine Arts
  - Substantially completed selective demolition.
  - Continued with technical submittals.
  - Completed pile installation
  - Concrete Footing and foundation continued to progress.
  - Wall patching was completed in advance of students and staff returning in September.
  - Structural steel erection commenced above the stage area and is working west toward the lobby. Truss steel work has commenced and is in progress.
  - Metal stud framing, MEP wall rough-in, and gypsum wall board installation is in progress in areas behind the stage.

- Pool
  - The gutter system has been installed. Old piping has been removed and floors and walls patched.
  - The waterproofing membrane has been installed and the water test process has commenced. This process will take approximately 10 days.

EXECUTIVE SUMMARY

Wetzel Road ES Roofing

- The roofing project is complete.

Transportation Center Renovations

- The project is complete.

PHASE 4

Longbranch ES

- The roofing project is complete.

Liverpool Public Library

- The library project associated with Phase 4 is complete.

NPE, WRE, DO Boiler Work

- This phase 4 project is now complete.

WRE Sitework

- This work is now complete and final closeout is in process.

Transportation Center Fuel Island Replacement

- This work is now complete.

30-DAY LOOK AHEAD

PHASE 3

Liverpool High School

- Athletics
    - Install coiling shutters
    - Complete punchlist work
    - Begin Exterior artificial turf surface
    - Complete systems commissioning and training
- Fine Arts

EXECUTIVE SUMMARY

- Complete concrete footings, foundations, and backfill
- Continue structural steel erection and truss construction
- Continue with technical submittals
- Continue metal stud and gyysum wallboard installation
- Commence efforts to temporarily enclose building, provide temporary heat

- Pool
  - Complete waterproof membrane water test
  - Continue construction of bench, rough in ductwork
  - Begin pool tile
  - Investigate existing pool mechanical, plumbing, and electrical systems scheduled to remain

Wetzel Road ES Roofing

- The project is complete.

Transportation Center Renovations

- The project is complete.

PHASE 4

Liverpool Public Library

- The project is complete.

NPE, WRE, District Office

- The project is complete.

LES, LMS, SRC

- The project is complete

WRE Sitework

- The project is complete.

Transportation Center Fuel Island Replacement

- The project is complete.

EXECUTIVE SUMMARY

Gymnasium Flooring, Bleachers, Wall pads, and equipment in place

EXECUTIVE SUMMARY

Athletics Fitness Room Equipment in Place

EXECUTIVE SUMMARY

Athletics Lobby Entrance Terrazzo Flooring in Progress

EXECUTIVE SUMMARY

Fine Arts Lobby / Entrance Foundations completed, New Structural Steel Erection in Progress

EXECUTIVE SUMMARY

Fine Arts Area New Lobby / Entrance Structural Steel Erection

EXECUTIVE SUMMARY

Auditorium Stage Area Steel Reinforcing, Truss Construction, and Foundation Walls in Progress

EXECUTIVE SUMMARY

Fine Arts Area Mezzanine Metal Studs, Gypsum Wallboard, and Door Frames in Progress

EXECUTIVE SUMMARY

Fine Arts Areas Masonry Infill, Metal Studs, Door Frames, Gypsum Drywall, Ductwork, Piping, and Electrical Rough in in Progress

EXECUTIVE SUMMARY

Pool New Waterproofing System Water Test in Progress

EXECUTIVE SUMMARY

Pool Floor and Wall Patching Completed, New Waterproofing System Installed

EXECUTIVE SUMMARY

Pool New Gutter System Installed

EXECUTIVE SUMMARY

Athletics Addition Main Entrance Sitework Substantially Completed

EXECUTIVE SUMMARY

Athletics Main Entrance – Go Warriors!

EXECUTIVE SUMMARY

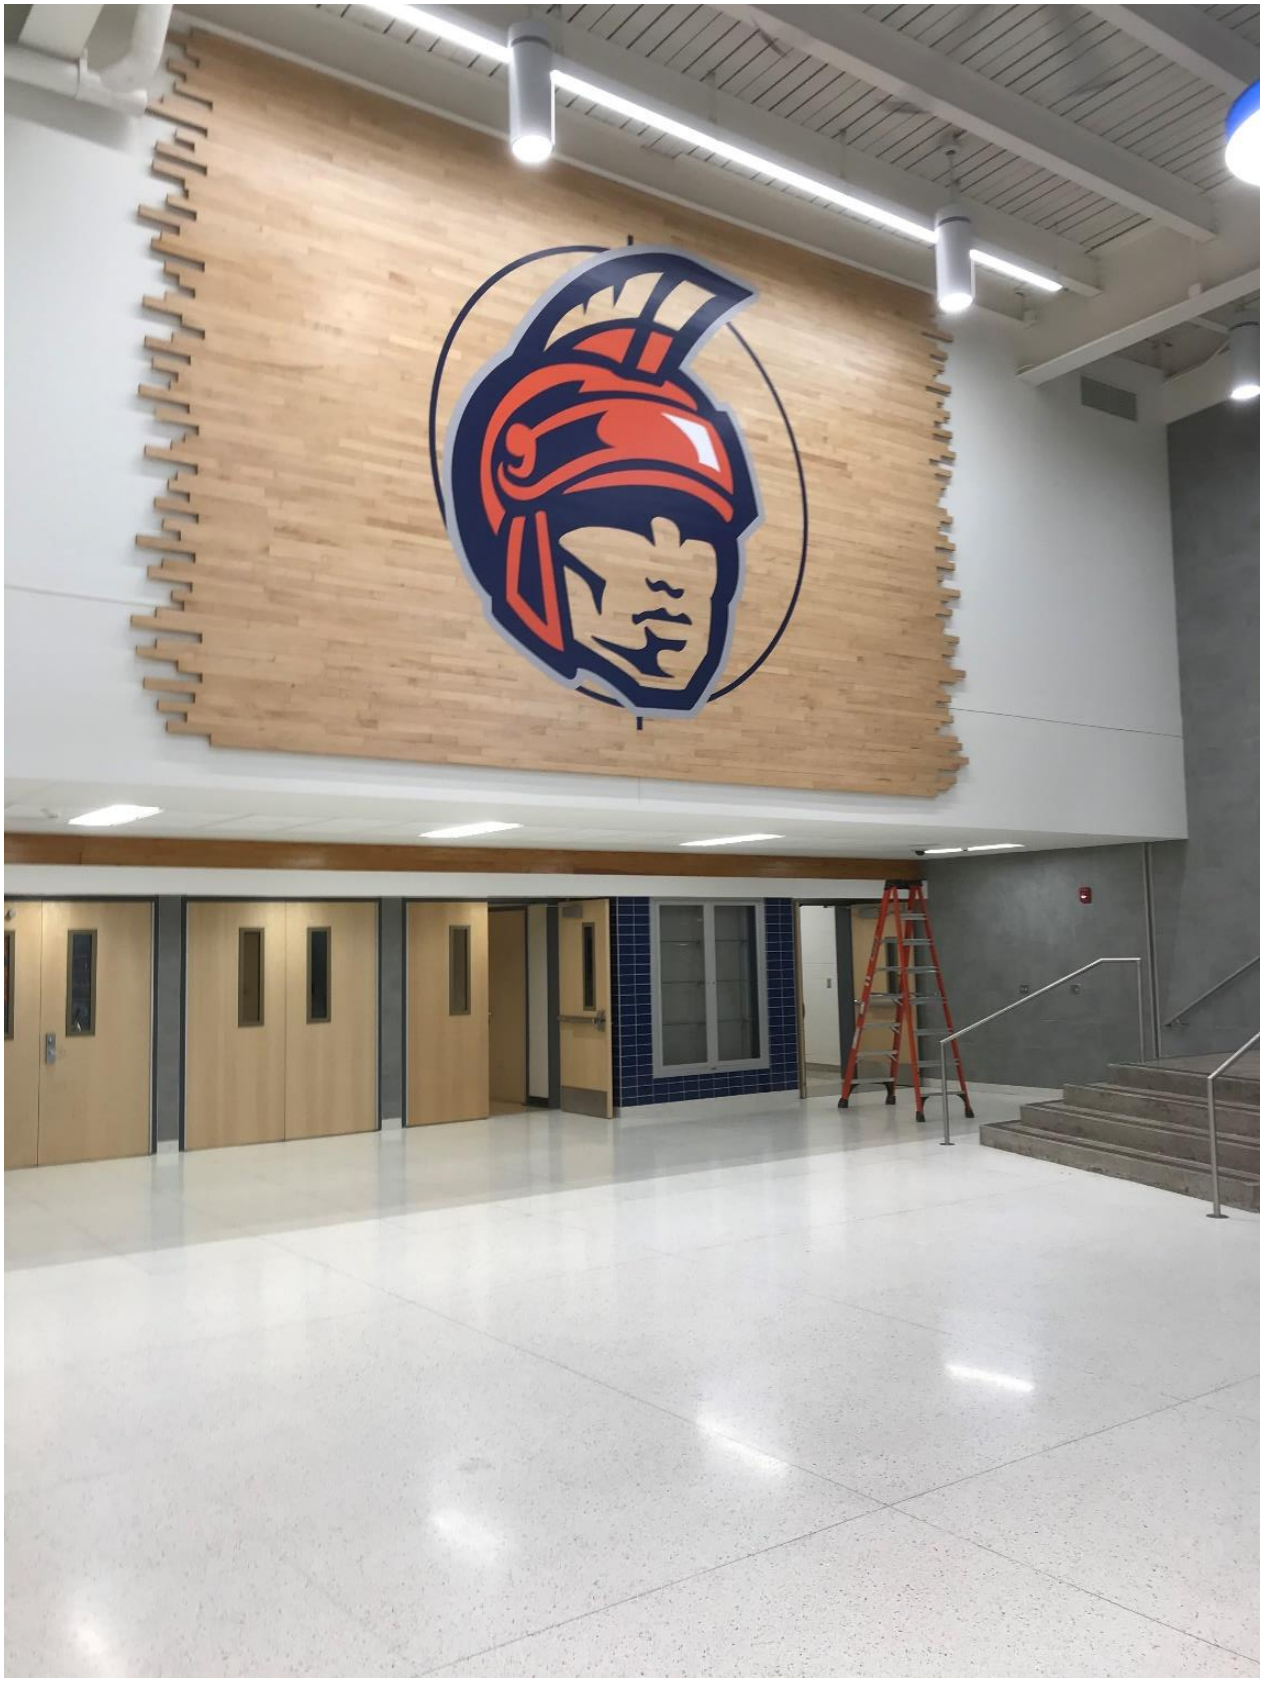

Athletics Area New Lobby Warrior Mural
